

DATA QUALITY ASSESSMENT - MASTER WORK PLAN

Belize Health Information System (BHIS) | Ministry of Health and Wellness

Project Period: January 19, 2026 - December 27, 2026 (50 weeks) | Version 0.1

#	Phase / Activity	Responsible	Start Date	End Date	Deliverable	Due Date
P1	PHASE 1: PREPARATION AND SCOPING (5 weeks: Jan 19 - Feb 22)					
1.1	Scoping and Methodology Development		Jan 19	Feb 22		
1.1.1	Identify and map all relevant stakeholders	Infostructure Lead	Jan 19	Jan 25		
1.1.2	Review and adapt WHO DQR methodology for Belize context	Infostructure Lead	Jan 26	Feb 8		
1.1.3	Draft core indicators and priority health data areas	Infostructure Lead	Feb 2	Feb 8	Indicator Selection Matrix	Feb 8
1.1.4	Alignment Sessions with key stakeholders (IDB, MOHW)	IL + DA + IDB + MOHW	Feb 2	Feb 8		
1.1.5	Confirm facility list for site assessment (8-10 facilities)	IL + MOHW	Feb 2	Feb 8		
1.1.6	Develop DQ Assessment Plan	Infostructure Lead	Feb 9	Feb 22	DQA Protocol	Feb 20
1.1.7	Validation Session of DQA Methodology and Plan	IL + DL + MOHW	Feb 15	Feb 22		
1.3	Data Requirements and Access		Feb 9	Feb 22		
1.3.1	Document data extraction requirements from BHIS	IL + Data Analyst	Feb 9	Feb 22	Data Access Requirements	Feb 8
1.3.2	Establish data access protocols and confidentiality agreements	IL + MOHW	Feb 15	Feb 22		
1.4	IS4H Situation Analysis		Jan 19	Feb 1		
1.4.1	Develop inventory of existing information products	IL + Data Analyst	Jan 19	Feb 1		
1.4.2	Develop inventory of data tools and applications	IL + Data Analyst	Jan 19	Feb 1		
1.4.4	Map the IT entity/unit (location, functions, reporting lines)	Data Analyst	Jan 19	Feb 1	IS4H Situation Analysis (Draft)	Feb 15
1.5	Information Needs Assessment - Initial Scoping		Jan 26	Feb 8		
1.5.1	Develop Information Needs Assessment questionnaire/interview guide	IL + Data Analyst	Jan 26	Feb 8	Info Needs Assessment Tool	Feb 8
1.5.2	Identify key informants for information needs interviews	Infostructure Lead	Feb 2	Feb 8		
P2	PHASE 2: DESK REVIEW (5 weeks: Feb 23 - Mar 29)					
2.1	Data Extraction and Preparation (1 week)		Feb 23	Feb 29		
2.1.1	Extract core indicator data from BHIS for selected time period	BHIS IT	Feb 23	Feb 29		
2.1.2	Prepare and adapt WHO desk review tool	IL + DA	Feb 23	Feb 29		
2.2	Data Quality Four-Dimensions Desk Review (2 weeks)		Mar 1	Mar 14		
2.2.1	Analyze data reporting completeness and data element completeness	IL + DA	Mar 1	Mar 7		
2.2.2	Assess timeliness of reporting at various levels	IL + DA	Mar 1	Mar 7		
2.2.3	Assess internal (logical, outliers) and temporal consistency	IL + DA	Mar 8	Mar 14		
2.2.4	Assess external consistency by comparing with data sources	IL + DA	Mar 8	Mar 14		
2.4	Health Data Workflow Mapping (1 week)		Feb 23	Feb 29		

2.4.4	Document current standards adoption status (ICD-10, HL7)	IL + DA + IT	Feb 23	Feb 29		
2.4.5	Assess CDEP readiness and document BHIS-CDEP data exchange requirements	IL + DA + IT	Feb 23	Feb 29		
2.5	Reporting and Validation (2 weeks)		Mar 15	Mar 29		
P3	PHASE 3: SITE ASSESSMENT (12 weeks: Mar 30 - Jun 14)					
3.1	Tool Development (2 weeks)		Mar 30	Apr 12		
3.1.1	Develop data verification forms for priority indicators	IL	Mar 30	Apr 5		
3.1.2	Create system assessment questionnaire	IL	Apr 6	Apr 10		
3.1.3	Pilot test tools and finalize	IL	Apr 10	Apr 12	Site Assessment Tools	Apr 12
3.2	Data Verification (4 weeks)		Apr 13	May 10		
3.2.1	Notify selected facilities and coordinate visit logistics	IL + MOHW	Apr 13	Apr 19		
3.2.2	Conduct site visits to Selected Facilities (incl. info needs interviews)	IL + DA	Apr 20	May 3		
3.2.3	Calculate verification factors and compile data verification findings	IL	May 4	May 10	Data Verification Report	May 10
3.3	System Assessment (4 weeks)		May 11	Jun 7		
3.3.1	Analyze system assessment data from facility visits	IL	May 11	May 24		
3.3.2	Conduct follow-up interviews with facility data managers	IL	May 25	May 31		
3.3.4	Compile System Assessment Report	IL	Jun 1	Jun 7	System Assessment Report	Jun 7
3.4	Information Needs Report Compilation		Jun 1	Jun 14	Info Needs Report (Draft)	Jun 7
P4	PHASE 4: ANALYSIS AND PLANNING (16 weeks: Jun 15 - Oct 4)					
4.1	Comprehensive Data Analysis (4 weeks)		Jun 15	Jul 12		
4.2	DQA Report Development (4 weeks)		Jul 13	Aug 9		
4.3	DQIP Development (4 weeks)		Aug 10	Sep 6	Root Cause Analysis	Sep 6
4.4	Stakeholder Consultations and Validation (3 weeks)		Sep 7	Sep 27		
4.5	Report Finalization (1 week)		Sep 28	Oct 4	DQA Report; DQIP; Info Needs (Final)	Oct 4
P5	PHASE 5: IMPLEMENTATION SUPPORT (13 weeks: Oct 5 - Dec 27)					
5.1	Standard Operating Procedures Development (4 weeks)		Oct 5	Nov 1	SOPs for DQ Assurance	Nov 1
5.2	Monitoring and Evaluation Framework (3 weeks)		Nov 2	Nov 22	M&E Framework for DQ	Nov 22
5.3	Data Quality Dashboard and Reporting Specifications (3 weeks)		Nov 23	Dec 13	Dashboard Specifications	Dec 13
5.5	Data Quality Training Plan (2 weeks)		Dec 14	Dec 27	Training Materials; Closeout Report	Dec 27

Project Period: January 19, 2026 - December 27, 2026 (50 weeks)

[illegible]

P3	PHASE 3: SITE ASSESSMENT	Phase	Mar 30	Jun 21
3.1.1	Develop data verification forms	Activity	Mar 30	Apr 12
3.1.2	Create system assessment questionnaire	Activity	Apr 06	Apr 12
3.1.3	Pilot test tools and finalize	Activity	Apr 06	Apr 12
3.2.1	Notify facilities and coordinate logistics	Activity	Apr 13	Apr 19
3.2.2	Conduct site visits to Selected Facilities	Activity	Apr 20	May 03
3.2.3	Calculate verification factors	Activity	May 04	May 10
3.3.1	Analyze system assessment data	Activity	May 11	May 24
3.3.2	Follow-up interviews with facility data managers	Activity	May 25	May 31
3.3.4	Compile System Assessment Report	Activity	Jun 01	Jun 07
M4	[KEY MEETING: Site Visit Debriefs]	Meeting	May 04	May 10
M5	[KEY MEETING: Steering Committee #2]	Meeting	Jun 01	Jun 07
P4	PHASE 4: ANALYSIS AND PLANNING	Phase	Jun 15	Oct 04
4.1	Comprehensive Data Analysis	Activity	Jun 15	Jul 12
4.2	DQA Report Development	Activity	Jul 13	Aug 09
4.3	DQIP Development	Activity	Aug 10	Sep 06
4.4	Stakeholder Consultations and Validation	Activity	Sep 07	Sep 27
4.5	Report Finalization	Activity	Sep 28	Oct 04
M6	[KEY MEETING: DQIP Validation Workshop]	Meeting	Sep 14	Sep 20
M7	[KEY MEETING: Steering Committee #3]	Meeting	Sep 28	Oct 04
P5	PHASE 5: IMPLEMENTATION SUPPORT	Phase	Oct 05	Jan 03
5.1	Standard Operating Procedures Development	Activity	Oct 05	Nov 01
5.2	Monitoring and Evaluation Framework	Activity	Nov 02	Nov 22
5.3	Dashboard and Reporting Specifications	Activity	Nov 23	Dec 13
5.5	Data Quality Training Plan	Activity	Dec 14	Jan 03
M8	[KEY MEETING: Training Workshop]	Meeting	Dec 21	Dec 27
M9	[KEY MEETING: Project Closeout]	Meeting	Dec 28	Jan 03
	[Add Meeting Here]	Meeting		
	[Add Meeting Here]	Meeting		
	[Add Meeting Here]	Meeting		
	[Add Meeting Here]	Meeting		
	[Add Meeting Here]	Meeting		


LEGEND

	Phase 1: Preparation and Scoping
	Phase 2: Desk Review
	Phase 3: Site Assessment
	Phase 4: Analysis and Planning
	Phase 5: Implementation Support
	Key Meeting / Milestone

WEEK REFERENCE

W1 = J.	W10 = Mar 23-29	W20 = May 25-31
W30 = .	W40 = Oct 12-18	W50 = Dec 21-27

[illegible]

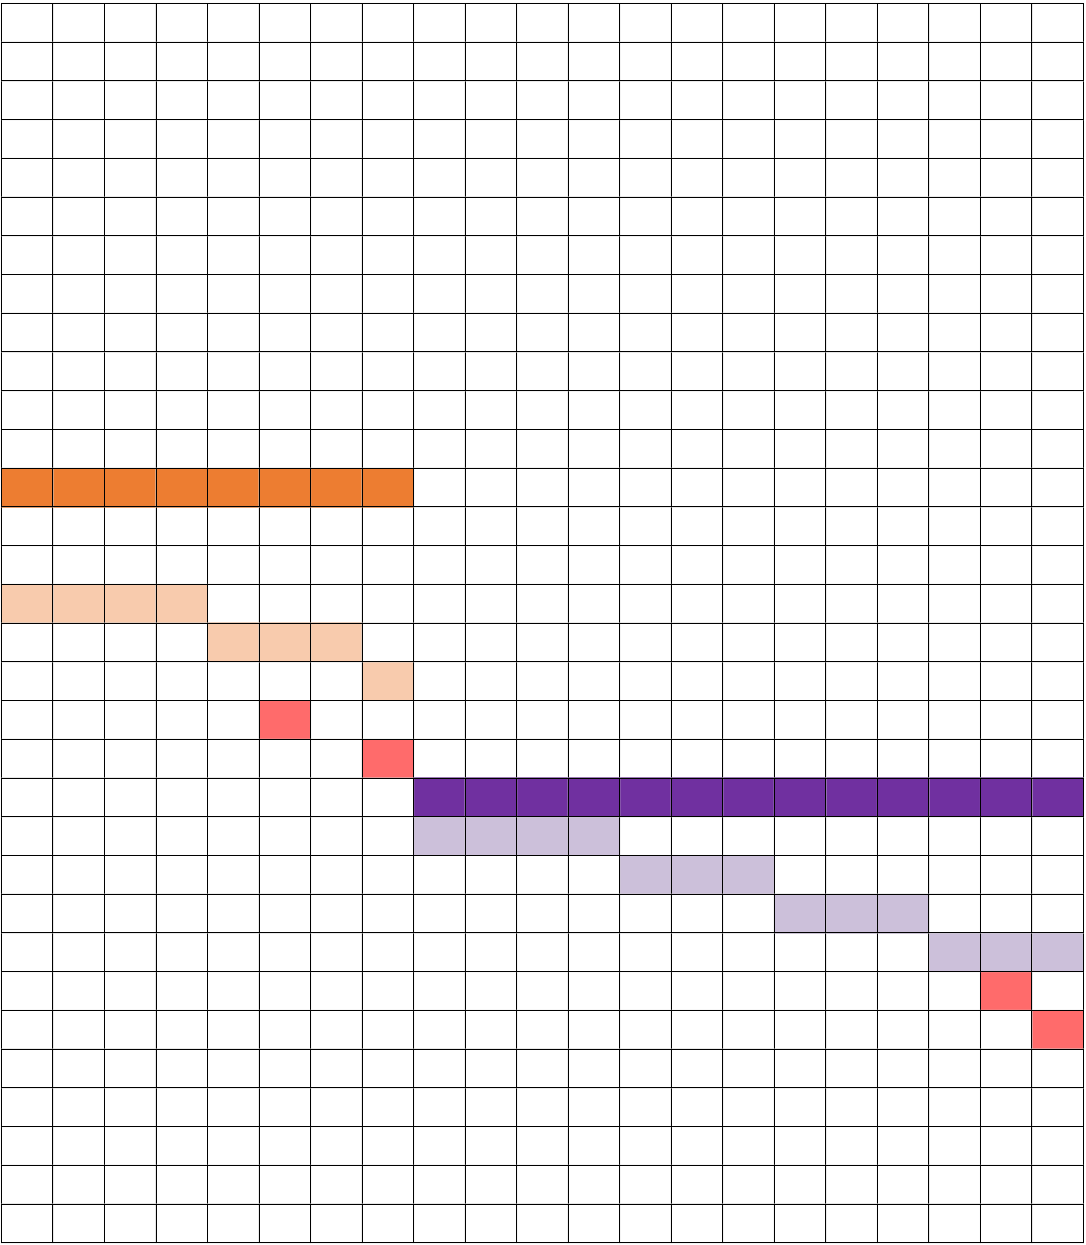

DQA DELIVERABLES TRACKER

#	Deliverable	Phase	Format	Due Date
1.1	Data Quality Assessment Protocol	Phase 1	Document (Word)	Feb 20, 2026
1.2	Data Quality Indicator Selection Matrix	Phase 1	Spreadsheet (Excel)	Feb 8, 2026
1.3	Data Access Requirements	Phase 1	Document (Word)	Feb 8, 2026
1.4	IS4H Situation Analysis Report (Draft)	Phase 1	Report (Word)	Feb 15, 2026
1.5	Information Needs Assessment Tool	Phase 1	Questionnaire (Word)	Feb 8, 2026
2.1	Desk Review Report	Phase 2	Report (Word + Excel)	Mar 29, 2026
2.2	Data Quality Scorecard (Baseline)	Phase 2	Spreadsheet (Excel)	Mar 29, 2026
2.3	IS4H Situation Analysis Report (Final)	Phase 2	Report (Word + Diagrams)	Mar 29, 2026
3.1	Site Assessment Tools	Phase 3	Forms (Word/CSPPro)	Apr 12, 2026
3.2	Data Verification Report	Phase 3	Report (Word + Excel)	May 10, 2026
3.3	System Assessment Report	Phase 3	Report (Word)	Jun 7, 2026
3.4	Information Needs Assessment Report (Draft)	Phase 3	Report (Word)	Jun 7, 2026
4.1	Comprehensive DQA Report	Phase 4	Report (Word + Annexes)	Oct 4, 2026
4.2	Root Cause Analysis	Phase 4	Document (Word)	Sep 6, 2026
4.3	Data Quality Improvement Plan (DQIP)	Phase 4	Plan (Word + Excel)	Oct 4, 2026
4.4	Information Needs Assessment Report (Final)	Phase 4	Report (Word)	Oct 4, 2026
5.1	SOPs for Data Quality Assurance	Phase 5	SOPs (Word)	Nov 1, 2026
5.2	Training Materials Package	Phase 5	Package (PPT + Word)	Dec 13, 2026
5.3	M&E Framework for Data Quality	Phase 5	Framework (Word)	Nov 22, 2026
5.4	Dashboard Specifications	Phase 5	Specifications (Word)	Dec 13, 2026
5.5	Project Closeout Report	Phase 5	Report (Word)	Dec 27, 2026

[illegible]
